

Sapwi Trails Community Park

Construction Update

September 11, 2018

Arboles Terrace

Clean-up continuing / final asphalt repairs / striping / irrigation and planting finalizing / electrical service on by Friday / boulder wall complete / move extra table to bike park.



Sapwi Trails Community Park

Construction Update

September 4, 2018

Arboles Terrace

Clean-up continuing / final asphalt repairs / striping in / irrigation and planting finalizing / electrical meter in - SCE to inspect / boulder wall in progress and decomposed granite install.



Sapwi Trails Community Park

Construction Update

August 28, 2018

Arboles Terrace

Clean-up continuing / final asphalt repairs and striping / irrigation and planting finalizing / electrical meter in - SCE to inspect / boulder wall at picnic area per site discussion.



Sapwi Trails Community Park

Construction Update

August 21, 2018

Arboles Terrace

Clean-up continuing / final asphalt repairs and striping / irrigation + planting finalizing / electrical meter in - SCE to inspect / CRPD sign in at Scenic/Arboles + plaques to be installed / boulder wall at picnic area per site discussion.



Sapwi Trails Community Park

Construction Update

August 14, 2018

Arboles Terrace

Clean-up continuing / irrigation + planting finalizing / water meter in / electrical meter in - SCE to inspect / CRPD installed park signs at Scenic/Arboles + to do rules signs by 8/24 + plaques / boulder wall at picnic area per site discussion.



Sapwi Trails Community Park

Construction Update

August 7, 2018

Arboles Terrace

Irrigation + planting finalizing / sewer in + water in meter pending / kiosk installed / clean-up started / CRPD to install park signs at Scenic/Arboles + rules signs - location spotted / boulder wall at picnic area per site discussion.




Sapwi Trails Community Park

Construction Update

July 24, 2018

Arboles Terrace

Irrigation + planting finalizing / sewer in + water in meter pending / kiosk to be installed / clean-up started / CRPD to install park signs at Scenic/Arboles - location spotted.

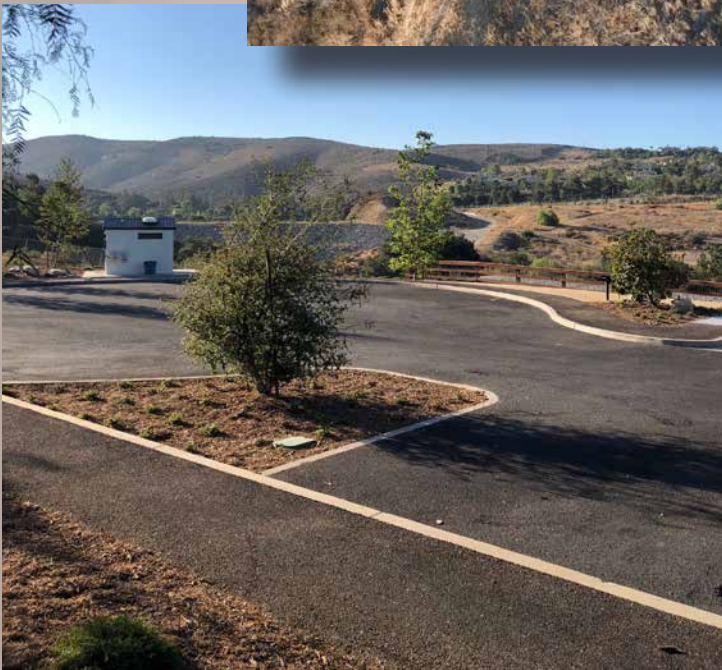

Sapwi Trails Community Park

Construction Update

July 17, 2018

Arboles Terrace

Irrigation and planting finalizing / sewer in and water in meter pending / kiosk to be installed.



Sapwi Trails Community Park

Construction Update

July 10, 2018

Arboles Terrace

Irrigation and planting finalizing / sewer in and water TBD working ahead of street work / kiosk to be installed.



Sapwi Trails Community Park

Construction Update

July 3, 2018

Arboles Terrace

Irrigation and planting finalizing / utility connection at street complete 1-2 weeks / located kiosk.



Sapwi Trails Community Park

Construction Update

June 26, 2018

Arboles Terrace

Irrigation and planting finalizing / utility connection at street complete 1-2 weeks / located kiosk.



Sapwi Trails Community Park

Construction Update

June 19, 2018

Arboles Terrace

Asphalt complete / irrigation and planting finalizing / utility connection at street complete 1-2 weeks



Sapwi Trails Community Park

Construction Update

June 12, 2018

Arboles Terrace

Asphalt this week / irrigation and planting finalizing / utility connection at street complete 1-2 weeks



Sapwi Trails Community Park

Construction Update

June 5, 2018

Arboles Terrace

Asphalt on hold due to utilities - to start week of June 11 / irrigation + planting finalizing / utility connection at street done by week of June 11



Sapwi Trails Community Park

Construction Update

May 29, 2018

Arboles Terrace

Asphalt on hold due to utilities / irrigation + planting finalizing / utility connection at street by end of May.




Sapwi Trails Community Park

Construction Update

May 29, 2018 (continued)

Arboles Terrace

Asphalt on hold due to utilities / irrigation + planting finalizing / utility connection at street by end of May.

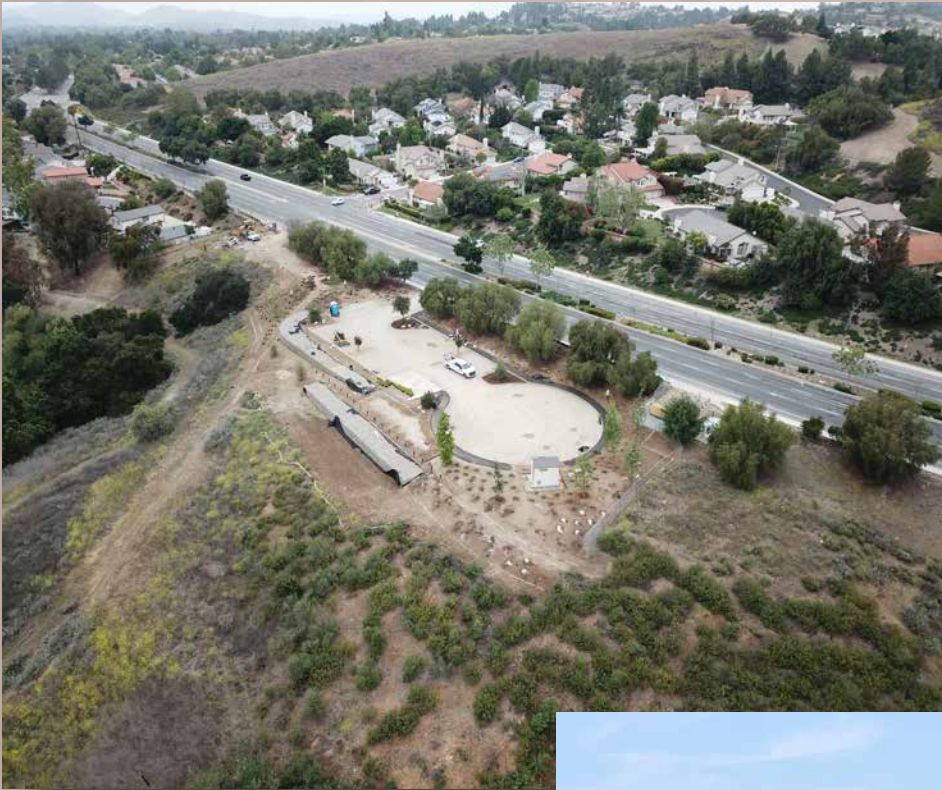

Sapwi Trails Community Park

Construction Update

May 22, 2018

Arboles Terrace

Asphalt complete 6-1 / irrigation + planting started / wall complete / utility connection at street by end of May.



Sapwi Trails Community Park

Construction Update

May 8, 2018

Arboles Terrace

Prepare subgrade - base this week / asphalt this week / irrigation started / correct wall elevation per drawings / utility connection at street by end of May.



Sapwi Trails Community Park

Construction Update

May 1, 2018

Arboles Terrace

Prepare subgrade - base this week / asphalt next week / irrigation started / correct wall elevation per drawings.



Sapwi Trails Community Park

Construction Update

April 24, 2018

Arboles Terrace

Prepare subgrade / irrigation started / review layout of picnic area - additional grading / API confirming wall layout



Sapwi Trails Community Park

Construction Update

April 17, 2018

Arboles Terrace

Prepare subgrade / parking lot curbing complete / trees installed / irrigation started / review layout of picnic area - additional grading



Sapwi Trails Community Park

Construction Update

April 10, 2018

Arboles Terrace

Prepare subgrade / parking lot curbing / utilities to street / tree install / irrigation started / review layout of picnic area / restroom installed 4/10



Sapwi Trails Community Park

Construction Update

April 3, 2018

Arboles Terrace

Prepare subgrade / parking lot curbing / utilities to street / tree install /
irrigation started / review layout of picnic area / restroom deliver-install 4/9



Sapwi Trails Community Park

Construction Update

March 20, 2018

Arboles Terrace

Prepare subgrade / parking lot curbing / utilities started / review layout of picnic area.



Sapwi Trails Community Park

Construction Update

March 13, 2018

Arboles Terrace

Grading complete / prepare subgrade / parking lot curbing / walls complete / utilities to start.



Sapwi Trails Community Park

Construction Update

March 6, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot curbing / wall #2 complete this week / utilities to start.



Sapwi Trails Community Park

Construction Update

March 6, 2018 (continued)

Arboles Terrace

Grading work / prepare subgrade / parking lot curbing / wall #2 complete this week / utilities to start.



Sapwi Trails Community Park

Construction Update

February 27, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot curbing / wall #2 in progress.



Sapwi Trails Community Park

Construction Update

February 20, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot / wall #2 construction started.



Sapwi Trails Community Park

Construction Update

February 13, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot / wall #1 construction started / restroom pad complete and tested.



Sapwi Trails Community Park

Construction Update

February 6, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot / wall construction started / restroom pad



Sapwi Trails Community Park

Construction Update

January 30, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot / materials onsite for wall / restroom pad



Sapwi Trails Community Park

Construction Update

January 23, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot / materials onsite for wall / restroom pad



Sapwi Trails Community Park

Construction Update

January 16, 2018

Arboles Terrace

Grading work / prepare subgrade / parking lot / materials onsite for wall



Sapwi Trails Community Park

Construction Update

November 21, 2017

Arboles Terrace

Grading work / prepare subgrade / parking lot layout

