

Sapwi Trails Community Park

Construction Update

September 18, 2018

Pedestrian Bridges at Creek

All bridges installed - minor grading at headwalls to flush trail connection and shift planks or replace to limit gaps all bridges.



Sapwi Trails Community Park

Construction Update

September 18, 2018

Pedestrian Bridges at Creek

All bridges installed - minor grading at headwalls to flush trail connection and shift planks or replace to limit gaps all bridges.



Sapwi Trails Community Park

Construction Update

September 4, 2018

Pedestrian Bridges at Creek

Bridge #2 headwall/beams poured - passed concrete test / bridges #1, #3, and #4 headwalls/beams to be poured on 9/6 / pending concrete testing approval, all bridges to be installed September 13/14, possibly sooner.



Sapwi Trails Community Park

Construction Update

August 28, 2018

Pedestrian Bridges at Creek

Bridge #1 poured (1) headwall/beam - rebar in progress / bridge #2 pouring headwall/beams today and tomorrow / bridge #3 (4) piles dug, (4) piles concrete in / bridge #4 (4) piles dug (4) piles concrete in progress / pending concrete testing approval / bridge #2 install week of 9/3 / bridges #1, #3 and #4 install week of 9/10.



Sapwi Trails Community Park

Construction Update

August 28, 2018

Pedestrian Bridges at Creek

Bridge #1 poured (1) headwall/beam - rebar in progress / bridge #2 pouring headwall/beams today and tomorrow / bridge #3 (4) piles dug, (4) piles concrete in / bridge #4 (4) piles dug (4) piles concrete in progress / pending concrete testing approval / bridge #2 install week of 9/3 / bridges #1, #3 and #4 install week of 9/10.



Sapwi Trails Community Park

Construction Update

August 21, 2018

Pedestrian Bridges at Creek

Bridges #1 and #2 (4) piles dug - (4) concrete in with headwall/beams in progress / bridge #3 (2) piles being dug, (2) piles concrete in / bridge #4 access and prep started drill piles late this week.




Sapwi Trails Community Park

Construction Update

August 14, 2018

Pedestrian Bridges at Creek

Bridge #2 (4) piles dug - (4) concrete in with headwall / bridge #3 (2) piles concrete in / bridge #1 started / driller down - will repair by Wednesday and continue work (2) piles per day / concrete delayed - continue work into next week.

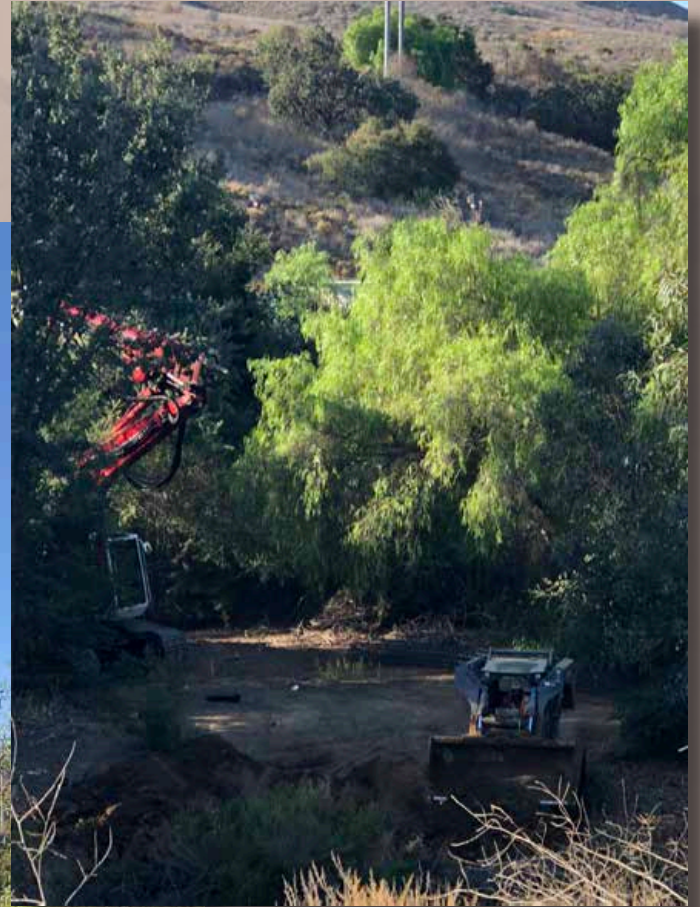

Sapwi Trails Community Park

Construction Update

August 7, 2018

Pedestrian Bridges at Creek

Driller on site. Bridge #2 (4) piles dug - (2) concrete in / bridge #3 (2) piles dug - concrete in / start bridge #1 and #4 this week - (2) piles per day / concrete complete by mid next week - cure period then bridges in late August.



Sapwi Trails Community Park

Construction Update

August 7, 2018

Pedestrian Bridges at Creek

Driller on site. Bridge #2 (4) piles dug - (2) concrete in / bridge #3 (2) piles dug - concrete in / start bridge #1 and #4 this week - (2) piles per day / concrete complete by mid next week - cure period then bridges in late August.



Sapwi Trails Community Park

Construction Update

July 31, 2018

Pedestrian Bridges at Creek

Crane and driller on site. Start bridge 2-3-4-1 (2) piles per day.



Sapwi Trails Community Park

Construction Update

July 10, 2018

Pedestrian Bridges at Creek

Layout started + rebar cages fabricated / work pending conc submittal.



Sapwi Trails Community Park

Construction Update

July 3, 2018

Pedestrian Bridges at Creek

Layout started + rebar cages fabricated / working pending conc submittal.



Sapwi Trails Community Park

Construction Update

April 24, 2018

Pedestrian Bridges at Creek

API working on detailed schedule to coordinate biologist/soils engineer field review and start work in coming weeks.



Sapwi Trails Community Park

Construction Update

February 6, 2018

Pedestrian Bridges at Creek

Pending FCS permits / tree trimming and clearing complete / bridge delivery mid-April / CRPD to verify permit status at end of February 2018 with FCS.



Sapwi Trails Community Park

Construction Update

February 6, 2018 (continued)

Pedestrian Bridges at Creek

Pending FCS permits / tree trimming and clearing complete / bridge delivery mid-April / CRPD to verify permit status at end of February 2018 with FCS.

