

Sapwi Trails Community Park

Construction Update

September 11, 2018

Westlake Upper Terrace

Clean-up continuing / sewer connected / timber curb installed / fix gaps at timber planters / trail loop finished, needs clean-up / driveway entry apron in, driveway pour today / upper driveway base/timbers in progress / PW in progress of trimming trees/ material in public right of way.



Sapwi Trails Community Park

Construction Update

August 21, 2018

Westlake Upper Terrace

Clean-up continuing / glider area to be clear by 8/17 / sewer pending + water meter installed / timber curb installed / fix gaps at timber planters / trail loop finished needs clean-up / driveway entry to be held until bridge installed / upper driveway / base and timbers in progress.



Sapwi Trails Community Park

Construction Update

August 14, 2018

Westlake Upper Terrace

Clean-up continuing / glider area to be clear by 8/17 / sewer pending + water meter installed / timber curb install / fix gaps at timber planters / trail loop finished - needs clean-up / driveway entry to be held until bridge installed / upper driveway base/timbers in progress.



Sapwi Trails Community Park

Construction Update

May 22, 2018

Westlake Upper Terrace

Utility connection at street by end of May / timber curb install / remaining pathways / continue cleanup / fix gaps at timber planters / trail loop finished needs cleanup / demo drive entryway + form - access to be closed from May 29-June 11 to TOSS.




Sapwi Trails Community Park

Construction Update

May 1, 2018

Westlake Upper Terrace

Utility run to street / timber curb install / remaining pathways / continue cleanup / fix gaps at timber planters / trail look this week / demo drive entryway + form.

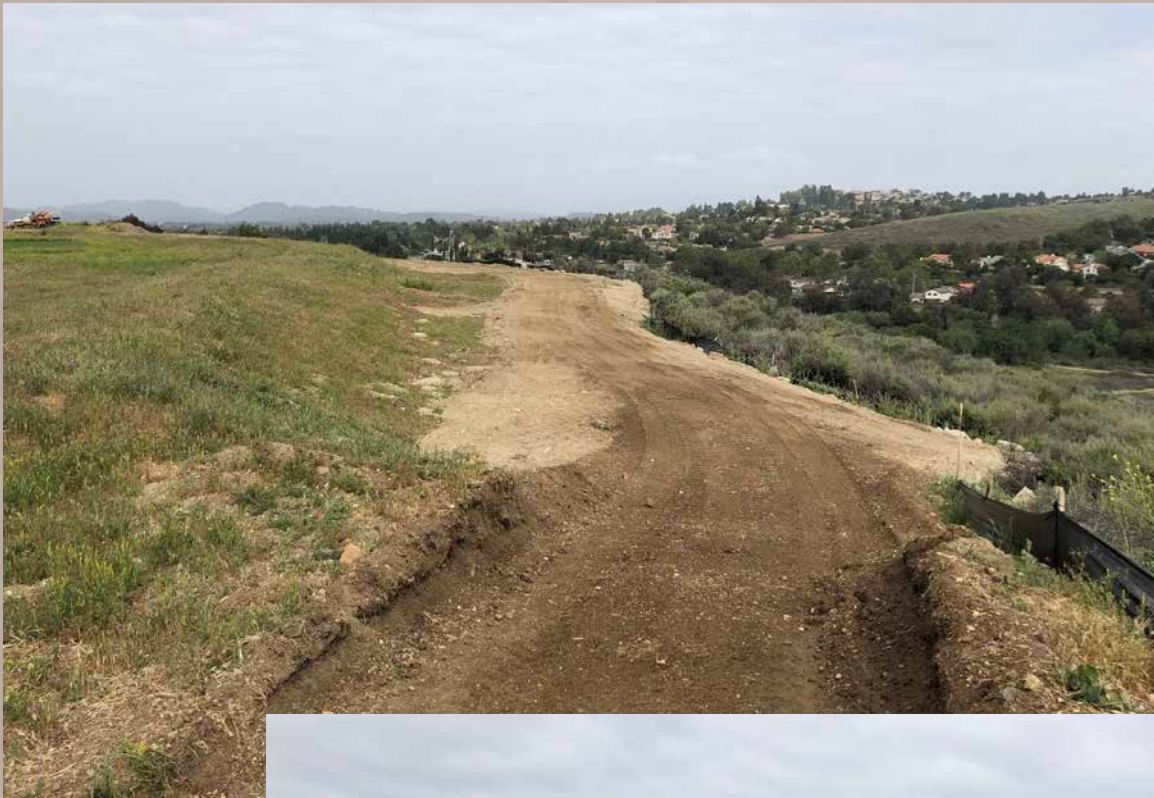

Sapwi Trails Community Park

Construction Update

April 24, 2018

Westlake Upper Terrace

Utility run to street / timber curb install / remaining pathways / trash and material offsite this week / fix gaps at timber planters.



Sapwi Trails Community Park

Construction Update

April 10, 2018

Westlake Upper Terrace

Utility run to street / timber curb install / remaining pathways / spoil removal / fix gaps at timber planters / base at road completed this week / restroom installed 4/10



Sapwi Trails Community Park

Construction Update

April 3, 2018

Westlake Upper Terrace

Utility run to street / timber curb install / remaining pathways / spoil removal / fix gaps at timber planters / base at road to start this week / restroom deliver-install 4/9 (re-open access for TOSS - Friday 4/13).




Sapwi Trails Community Park

Construction Update

March 6, 2018

Westlake Upper Terrace

Utility run at restroom to street / entry drive cut - timber curb install / remaining pathways / spoil removal / fix gaps at timber planters / base at restroom / base at road to be installed when utility run complete.

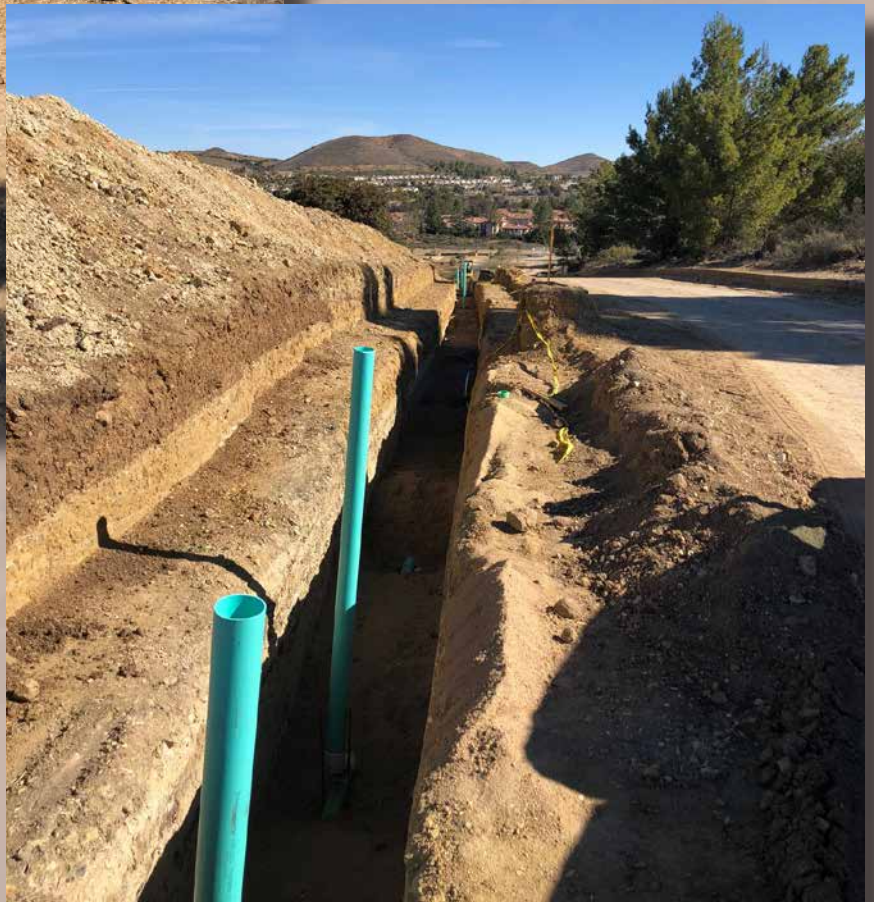

Sapwi Trails Community Park

Construction Update

February 27, 2018

Westlake Upper Terrace

Utility run at restroom to street / entry drive cut - timber curb install / remaining pathways / screening dirt for bike area



Sapwi Trails Community Park

Construction Update

February 20, 2018

Westlake Upper Terrace

Start utility run at restroom to street / entry drive cut - timber curb install / remaining pathways.



Sapwi Trails Community Park

Construction Update

February 13, 2018

Westlake Upper Terrace

Start utility run at restroom to street / grade entry drive / remaining pathways



Sapwi Trails Community Park

Construction Update

February 6, 2018

Westlake Upper Terrace

Start utility run at restroom to street / grade entry drive / remaining pathways



Sapwi Trails Community Park

Construction Update

January 23, 2018

Westlake Upper Terrace

Prepare subgrade / parking lot / timber curbs / tree install / over excavate restroom / ADA parking / on hold for restroom utility run



Sapwi Trails Community Park

Construction Update

January 16, 2018

Westlake Upper Terrace

Prepare subgrade / parking lot / timber curbs / tree install / over excavate restroom / ADA parking



Sapwi Trails Community Park

Construction Update

January 2, 2018

Westlake Upper Terrace

Prepare subgrade / parking lot / timber curbs / tree install



Sapwi Trails Community Park

Construction Update

December 5, 2017

Westlake Upper Terrace

Grading work area / prepare subgrade / parking lot layout.



Sapwi Trails Community Park

Construction Update

November 28, 2017

Westlake Upper Terrace

Grading work area; prepare subgrade; parking lot layout.



Sapwi Trails Community Park

Construction Update

November 21, 2017

Westlake Upper Terrace

Grading work; prepare subgrade; parking lot layout.

